


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Calendar	Qtr 2, 2012		Qtr 3, 2012			Qtr 4, 2012			Qtr 1, 2013		
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	
Norwottuck Trail Pedestrian Bridge over !																	
Milestones																	
1000	Notice to Proceed	0	25-Jun-12		78	7-Day Workweek											
1150	Open Bridge	0		02-Oct-12	85	7-Day Workweek											
1160	Final Acceptance	0		09-Oct-12	78	7-Day Workweek											
Preconstruction																	
1020	Steel Shop Drawings Submittal & Review	45	29-May-12 A	18-Jun-12 A		Amherst 5 Day Work											
1010	Subcontracts	20	12-Jun-12 A	16-Jun-12 A		Amherst 5 Day Work											
1030	Steel Fabrication & Delivery	60	19-Jun-12 A	03-Aug-12	56	Amherst 5 Day Work											
Construction																	
1040	Site Preparation	5	06-Aug-12	10-Aug-12	56	Amherst 5 Day Work											
1090	Fab Steel on Ground	5	06-Aug-12	10-Aug-12	76	Amherst 5 Day Work											
1050	Stone Dust Pathway	5	13-Aug-12	17-Aug-12	56	Amherst 5 Day Work											
1060	Bridge Demolition	5	20-Aug-12	24-Aug-12	56	Amherst 5 Day Work											
1070	Prepare New Bridge Seats	5	27-Aug-12	31-Aug-12	56	Amherst 5 Day Work											
1080	Cure Time for Bridge Seats	7	01-Sep-12	07-Sep-12	80	7-Day Workweek											
1100	Erect Steel	3	07-Sep-12	12-Sep-12	56	Amherst 5 Day Work											
1110	Construct Railings	7	12-Sep-12	21-Sep-12	56	Amherst 5 Day Work											
1120	Pave/Cleanup	2	21-Sep-12	25-Sep-12	56	Amherst 5 Day Work											
1130	Remove Stone Dust Pathway	2	25-Sep-12	27-Sep-12	56	Amherst 5 Day Work											
1140	Clean up/Demobilize	3	27-Sep-12	02-Oct-12	56	Amherst 5 Day Work											
1170	Punchlist	5	02-Oct-12	09-Oct-12	56	Amherst 5 Day Work											

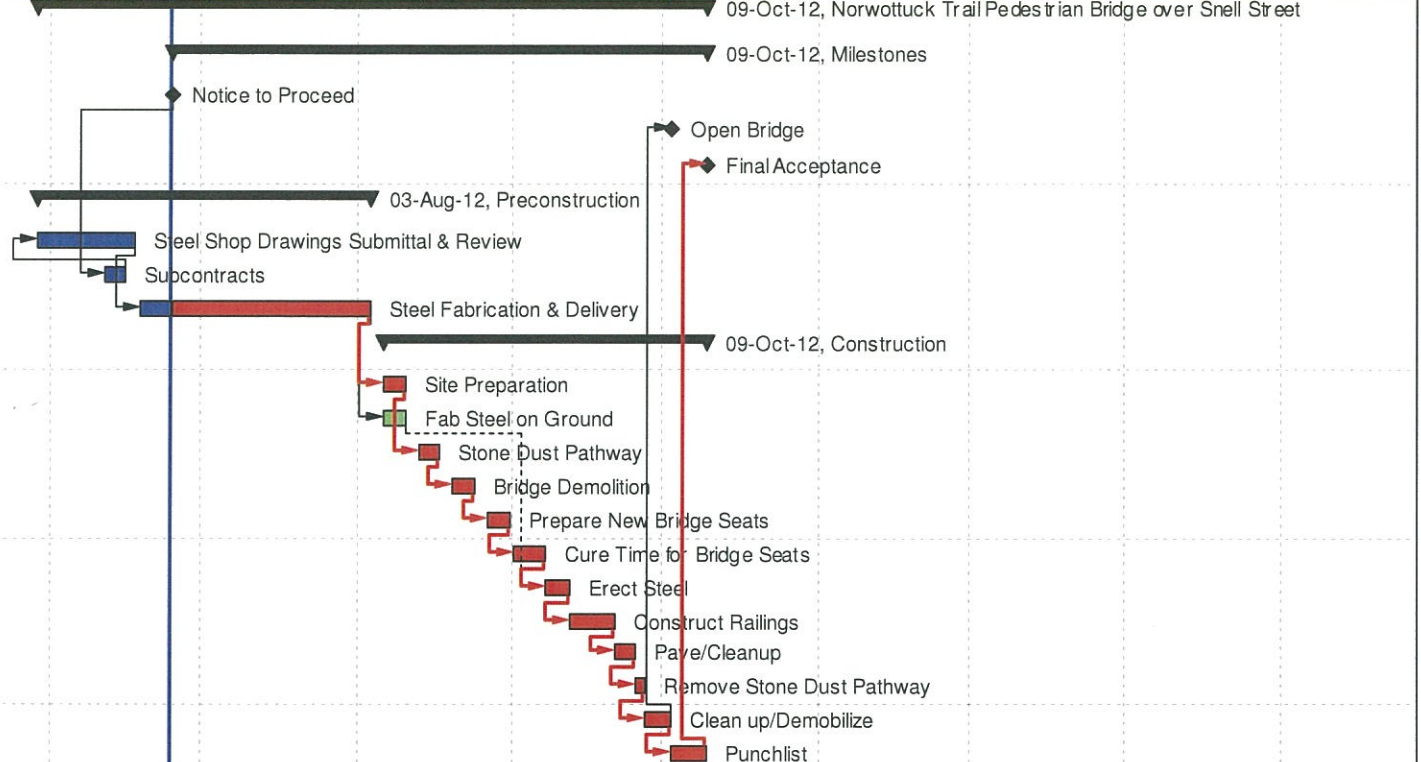

█ Actual Work
 █ Critical Remaining Work
 Summary
 Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
25-Jun-12	Norwottuck Trail Pedestrian Bridge - Amherst, MA		
	Update 001		
