


Project: Project1 Date: Sat 3/17/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

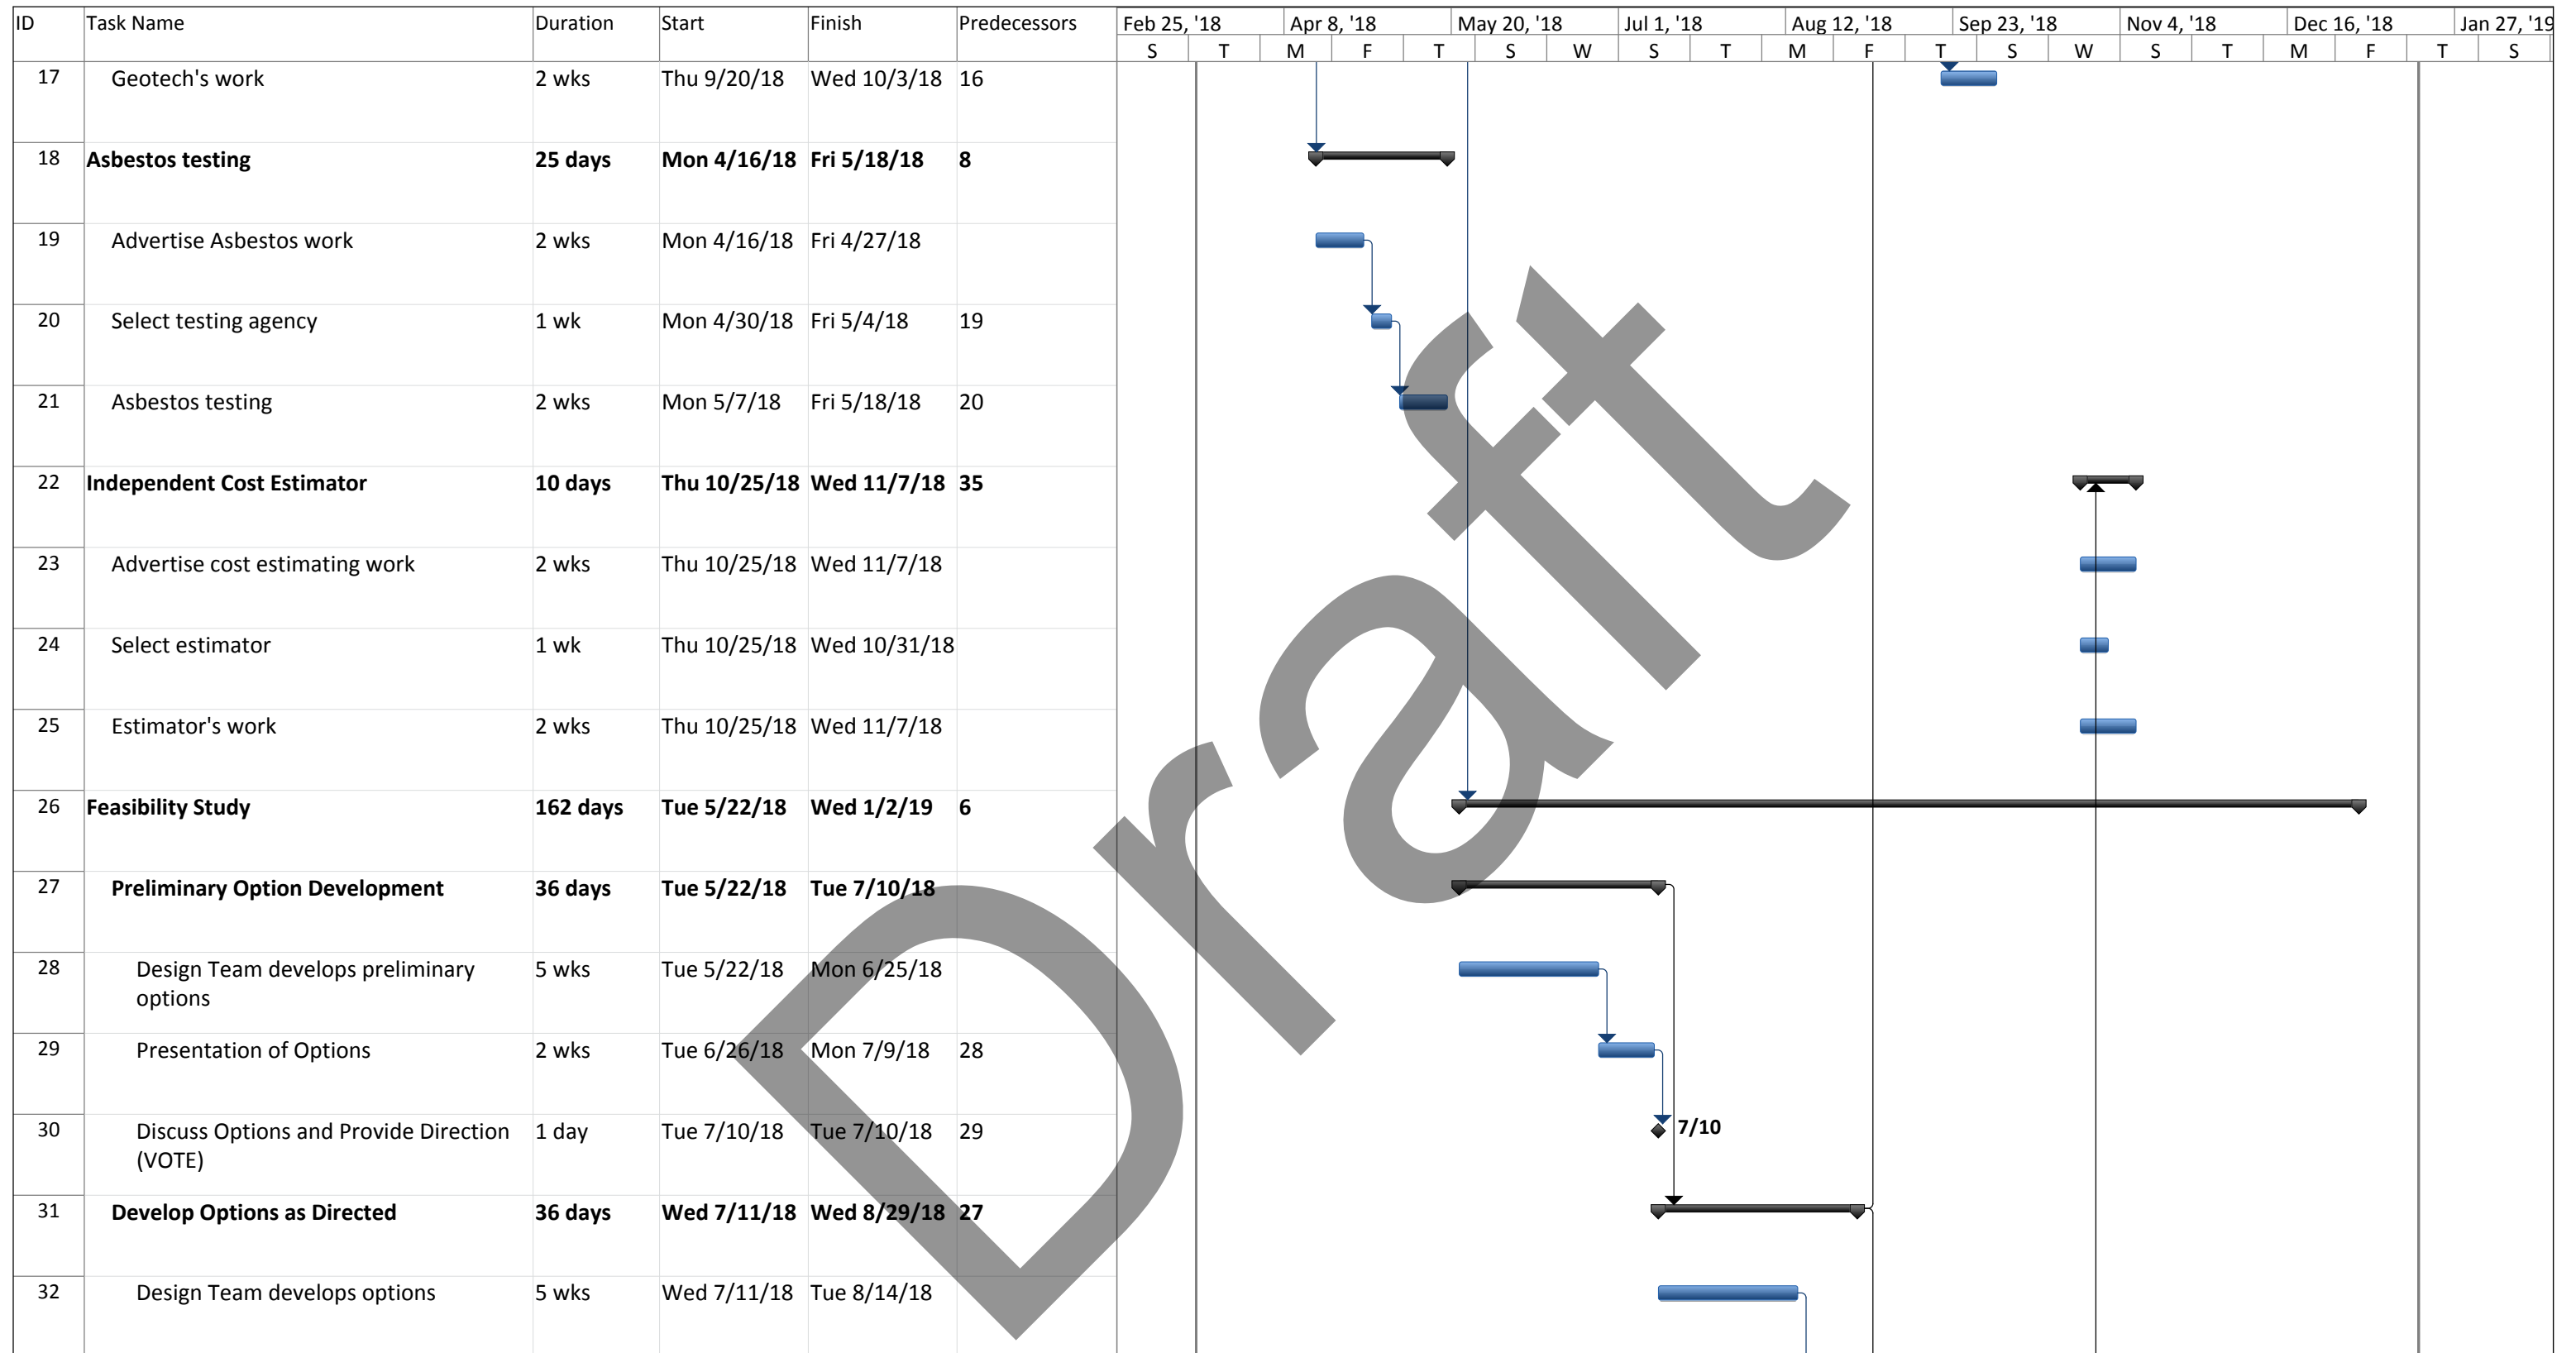

Project: Project1 Date: Sat 3/17/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors	Feb 25, '18		Apr 8, '18		May 20, '18		Jul 1, '18		Aug 12, '18		Sep 23, '18		Nov 4, '18		Dec 16, '18		Jan 27, '19	
						S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F
33	Presentation of Options	2 wks	Wed 8/15/18	Tue 8/28/18	32																		
34	Discuss Options and Provide Direction (VOTE)	1 day	Wed 8/29/18	Wed 8/29/18	33																		
35	Refine Options with Cost Estimates	40 days	Thu 8/30/18	Wed 10/24/18	31																		
36	Design Team refines Options and Cost Estimates	6 wks	Thu 8/30/18	Wed 10/10/18																			
37	Present Options	2 wks	Thu 10/11/18	Wed 10/24/18	36																		
38	Discuss Options and Provide Direction (VOTE)	0 days	Wed 10/24/18	Wed 10/24/18	37																		
39	Reconcile Cost Estimates	2 wks	Thu 8/30/18	Wed 9/12/18																			
40	Finalize Options with Recommendations	50 days	Thu 10/25/18	Wed 1/2/19	35																		
41	Design Team finalizes options and recommendations	6 wks	Thu 10/25/18	Wed 12/5/18																			
42	Present Options and Recommendations	2 wks	Thu 12/6/18	Wed 12/19/18	41																		
43	Deliver final report	2 wks	Thu 12/20/18	Wed 1/2/19	42																		
44	Discuss and review final report	11 days	Thu 1/3/19	Thu 1/17/19	40																		
45	Review final report	2 wks	Thu 1/3/19	Wed 1/16/19																			
46	Vote to send Report and Recommendations to School Committee	1 day	Thu 1/17/19	Thu 1/17/19	45																		

Project: Project1 Date: Sat 3/17/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
